ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1			**Analiza zahtjeva**	**11 days**	**Fri 07/06/24**	**Fri 21/06/24**		**Analitičar poslovn**
2			Prikupljanje zahtjeva	5 days	Fri 07/06/24	Thu 13/06/24		Analitičar poslovnih
3			Analiza funkcionalnih zahtjeva	3 days	Fri 14/06/24	Tue 18/06/24	2	Analitičar poslovnih zahtjeva
4			Analiza nefunkcionalnih zahtjeva	3 days	Wed 19/06/24	Fri 21/06/24	3	Analitičar poslovnih zahtjeva
5			**Dizajn sustava**	**14 days**	**Mon 24/06/2**	**Thu 11/07/24**	**1**	**Database adminis**
6			Arhitektura sustava	5 days	Mon 24/06/24	Fri 28/06/24		Softverski arhitekt
7			Dizajn baze podataka	5 days	Mon 01/07/24	Fri 05/07/24	6	Database administrator
8			Dizajn korisničkog sučelja	4 days	Mon 08/07/24	Thu 11/07/24	7	UX/UI dizajner
9			**Razvoj sustava**	**50 days**	**Fri 12/07/24**	**Thu 19/09/24**	**5**	**Backend develop**
10			Backend	20 days	Fri 12/07/24	Thu 08/08/24		Backend develope
11			Frontend	20 days	Fri 09/08/24	Thu 05/09/24	10	Frontend develop
12			Integracija sustava	10 days	Fri 06/09/24	Thu 19/09/24	11	Backend developer,Fronte
13			**Testiranje sustava**	**20 days**	**Fri 20/09/24**	**Thu 17/10/24**	**9**	**QA inženjer**
14			Pisanje testnih scenarija	5 days	Fri 20/09/24	Thu 26/09/24		QA inženjer

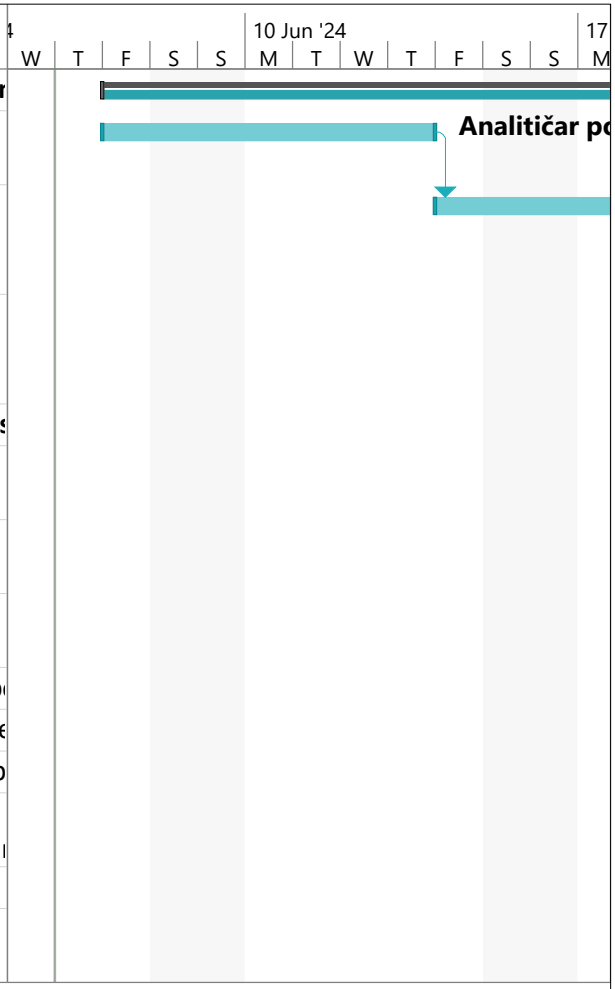

Project: plan projekta
Date: Thu 06/06/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
15			Izvođenje testiranja	10 days	Fri 27/09/24	Thu 10/10/24	14	QA inženjer
16			Izvještavanje o greškama	5 days	Fri 11/10/24	Thu 17/10/24	15	QA inženjer
17			**Implementacija**	**12 days**	**Fri 18/10/24**	**Mon 04/11/2**	**13**	**Database adminis**
18			Postavljanje na server	3 days	Fri 18/10/24	Tue 22/10/24		DevOps inženjer
19			Migracija podataka	4 days	Wed 23/10/24	Mon 28/10/24	18	Database administrator
20			Konačno testiranje	5 days	Tue 29/10/24	Mon 04/11/24	19	QA inženjer
21			**Obuka korisnika**	**15 days**	**Tue 05/11/2**	**Mon 25/11/2**	**17**	**Stručnjak za obuk**
22			Izrada materijala za obuku	5 days	Tue 05/11/24	Mon 11/11/24		Stručnjak za obuku
23			Obuka osoblja	10 days	Tue 12/11/24	Mon 25/11/2	22	Stručnjak za obuk

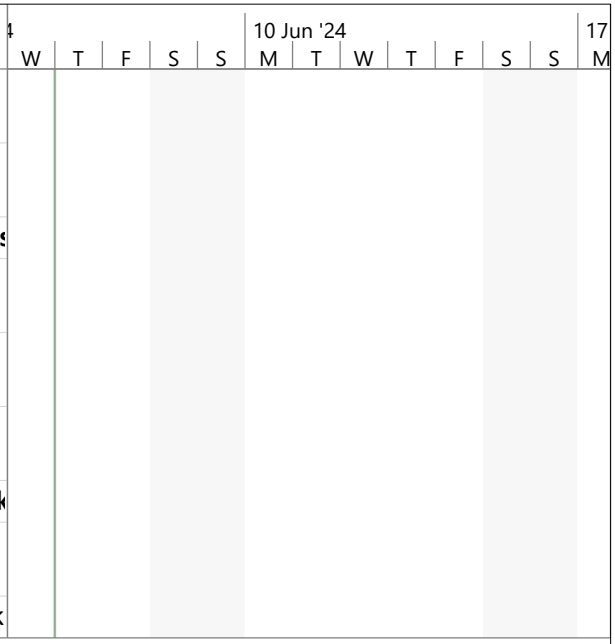

Project: plan projekta
Date: Thu 06/06/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

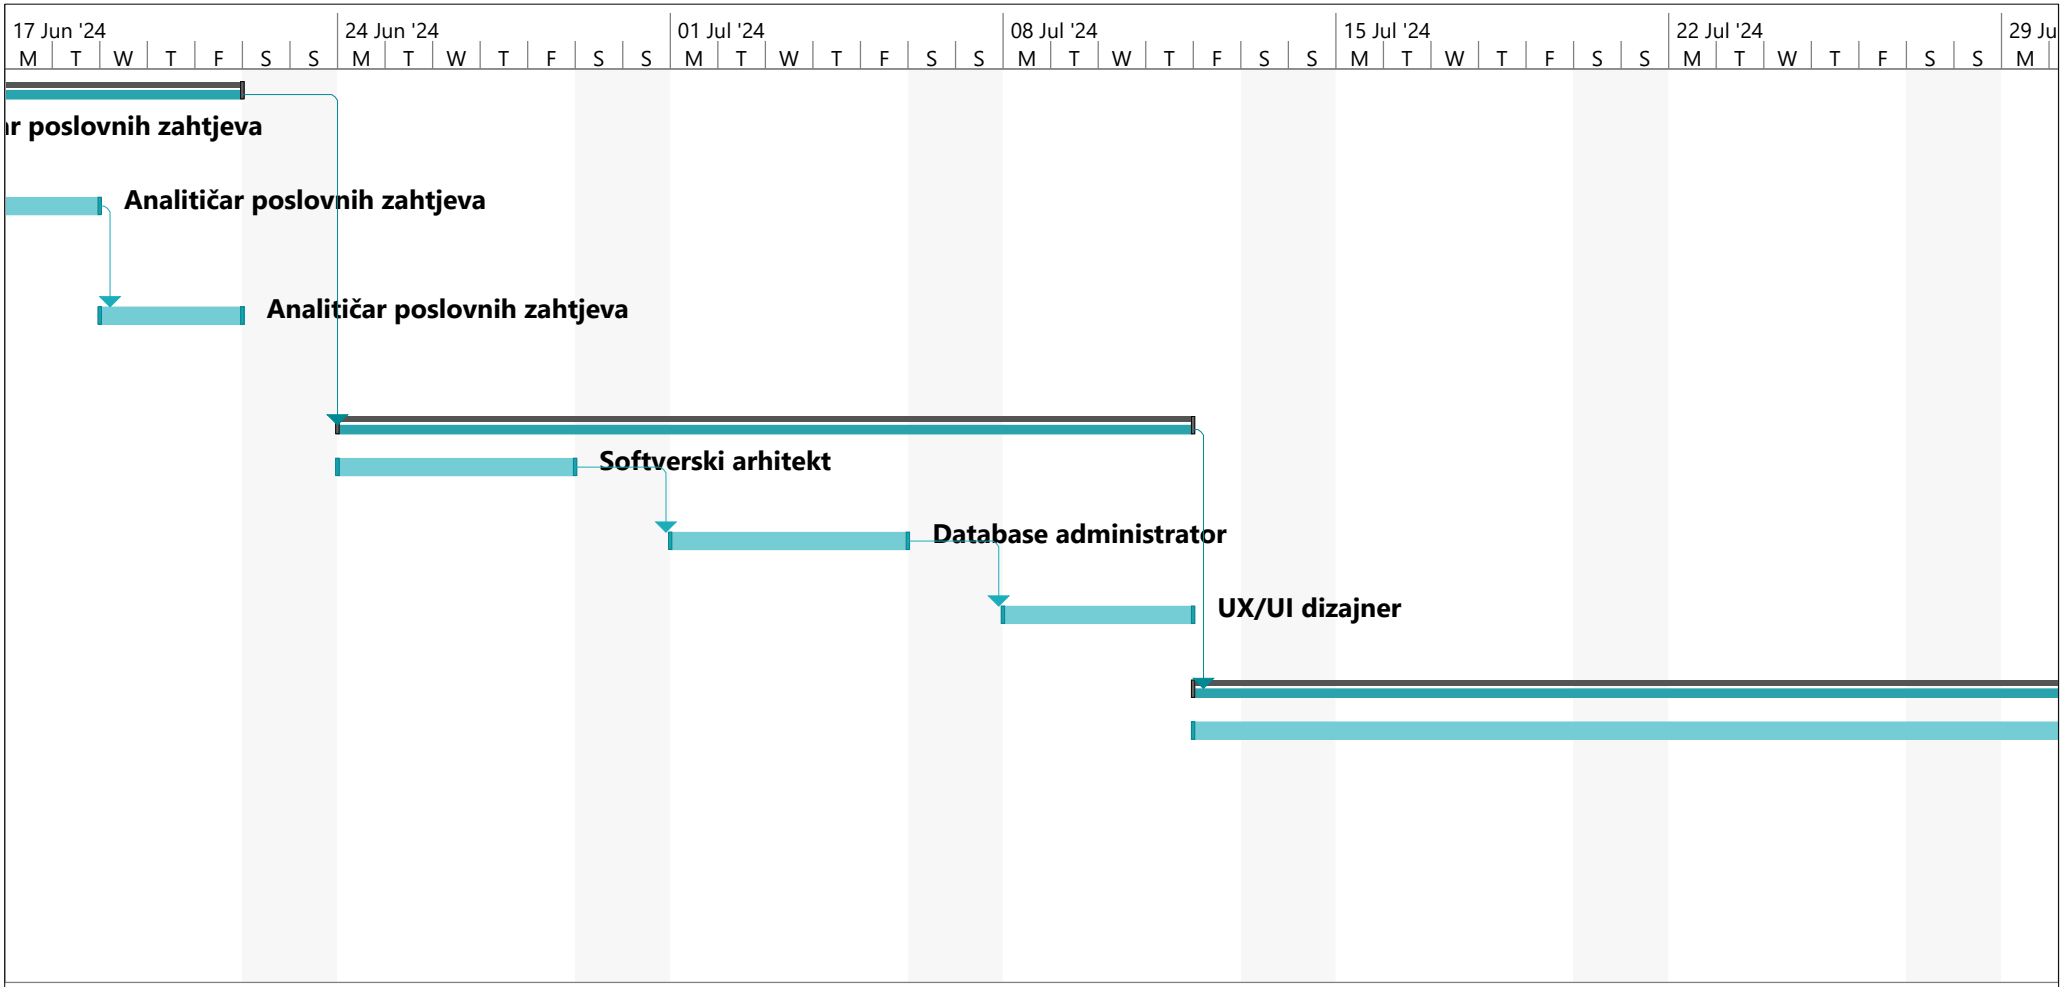

Project: plan projekta
Date: Thu 06/06/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

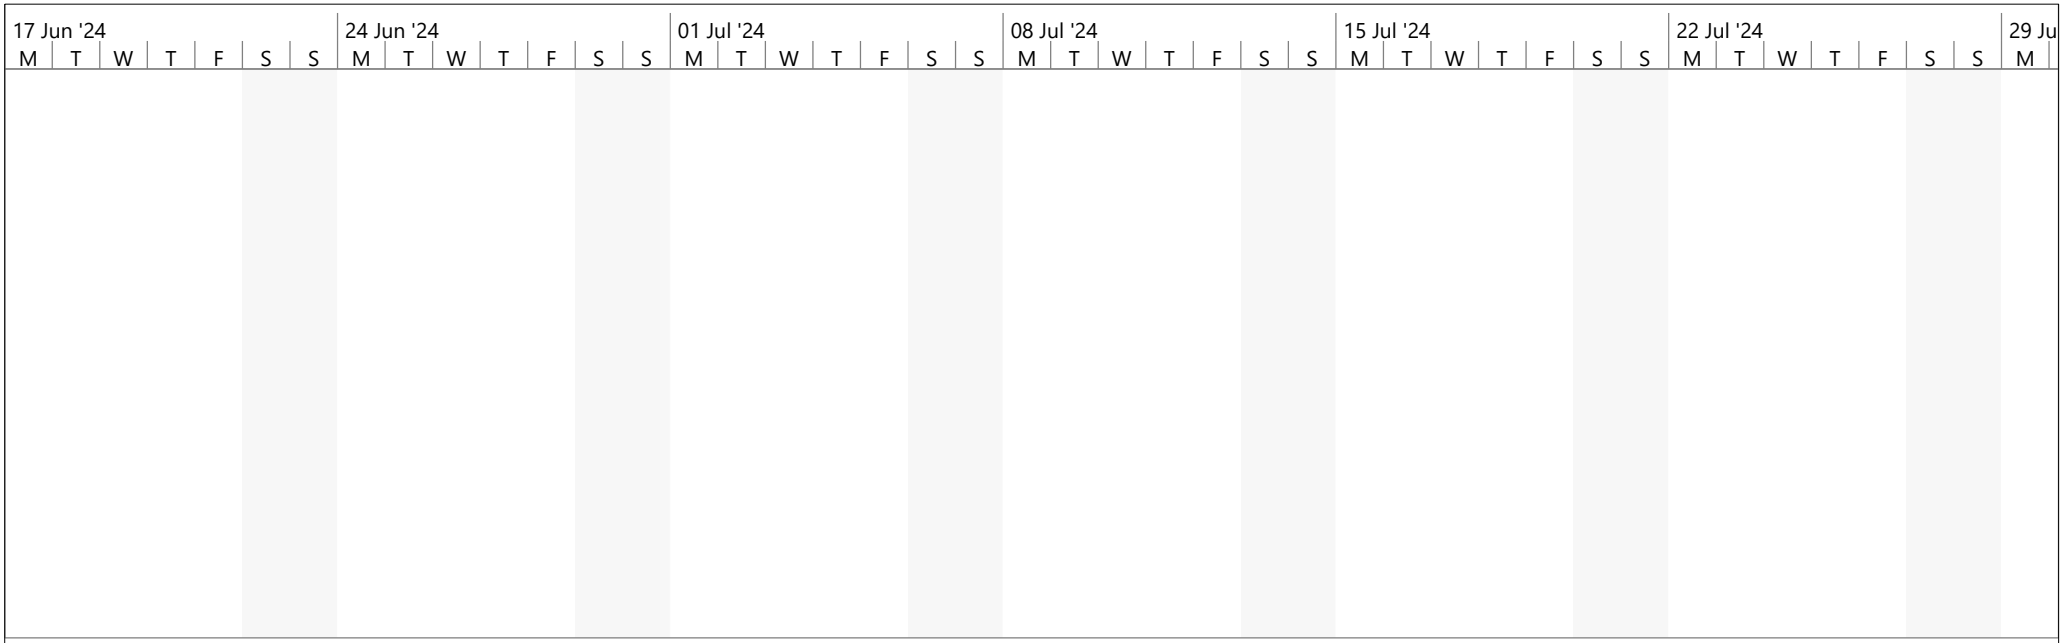

Project: plan projekta
Date: Thu 06/06/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

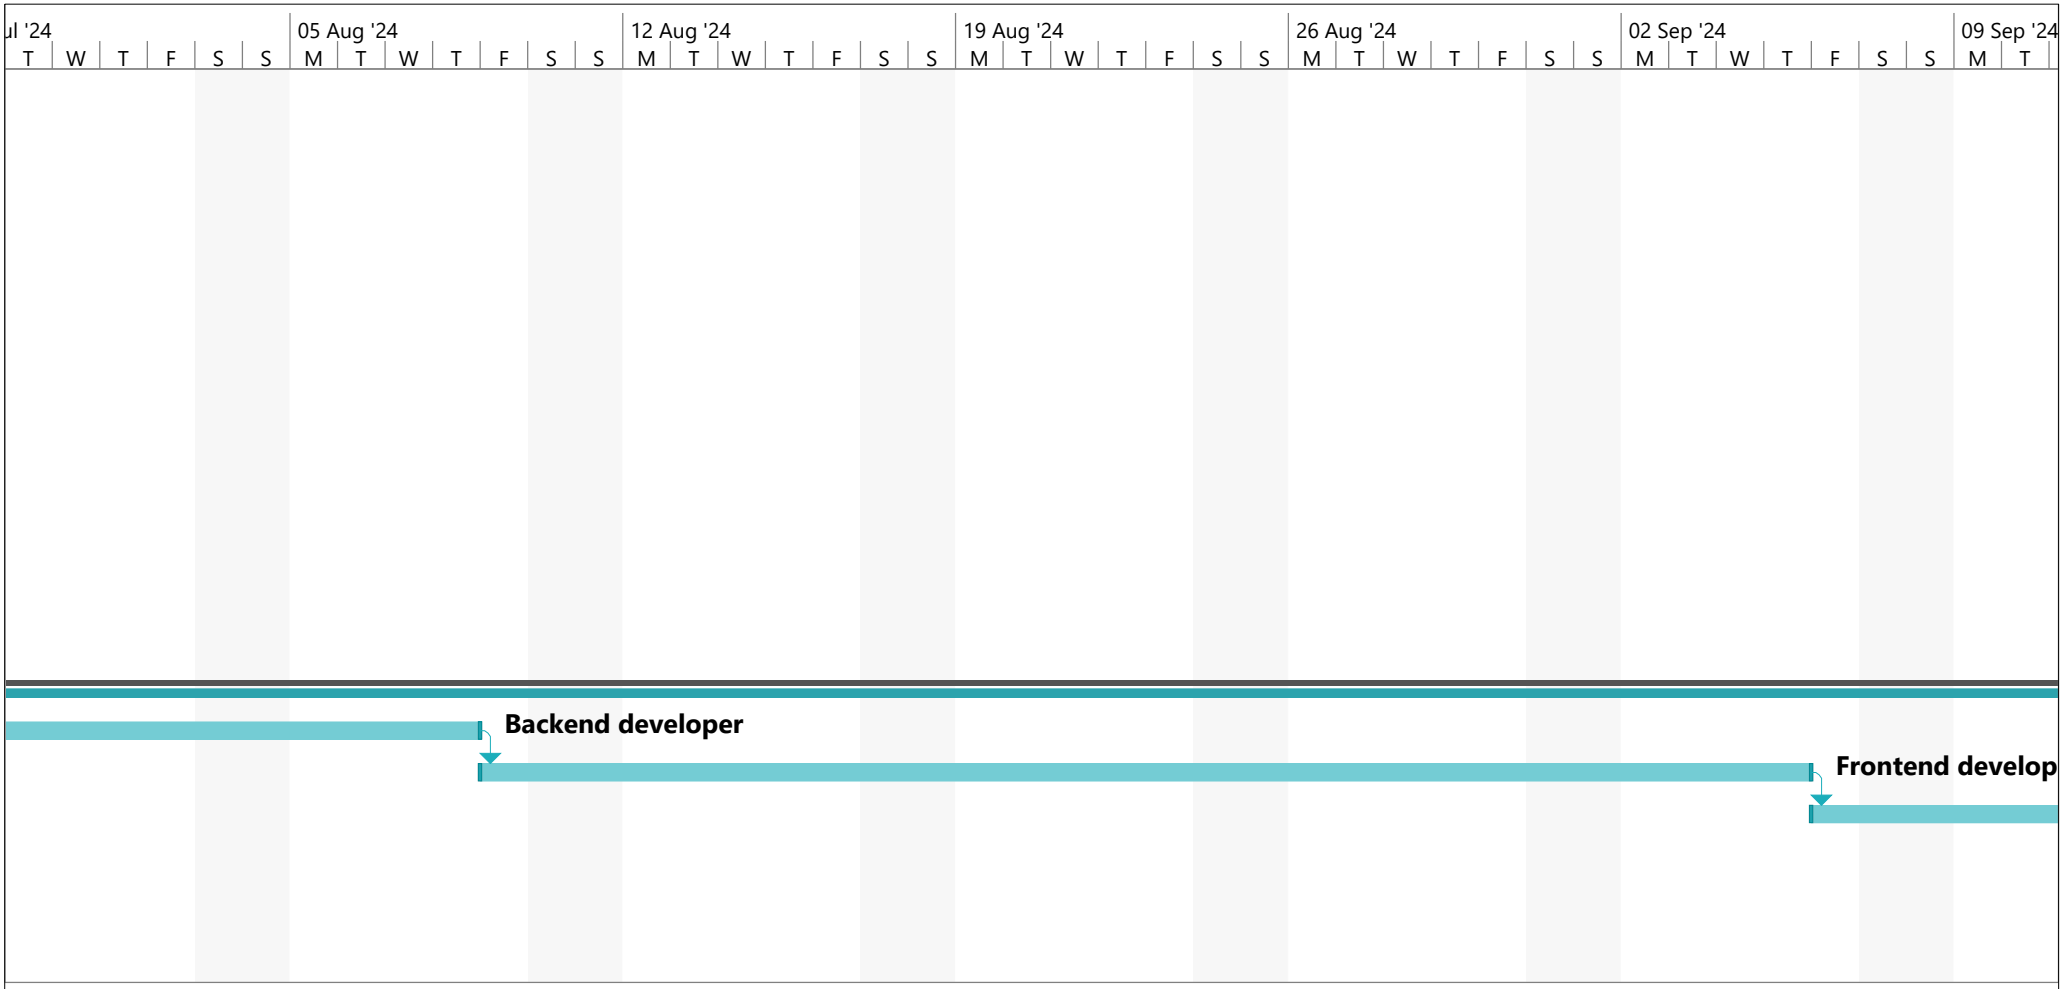

Project: plan projekta
Date: Thu 06/06/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

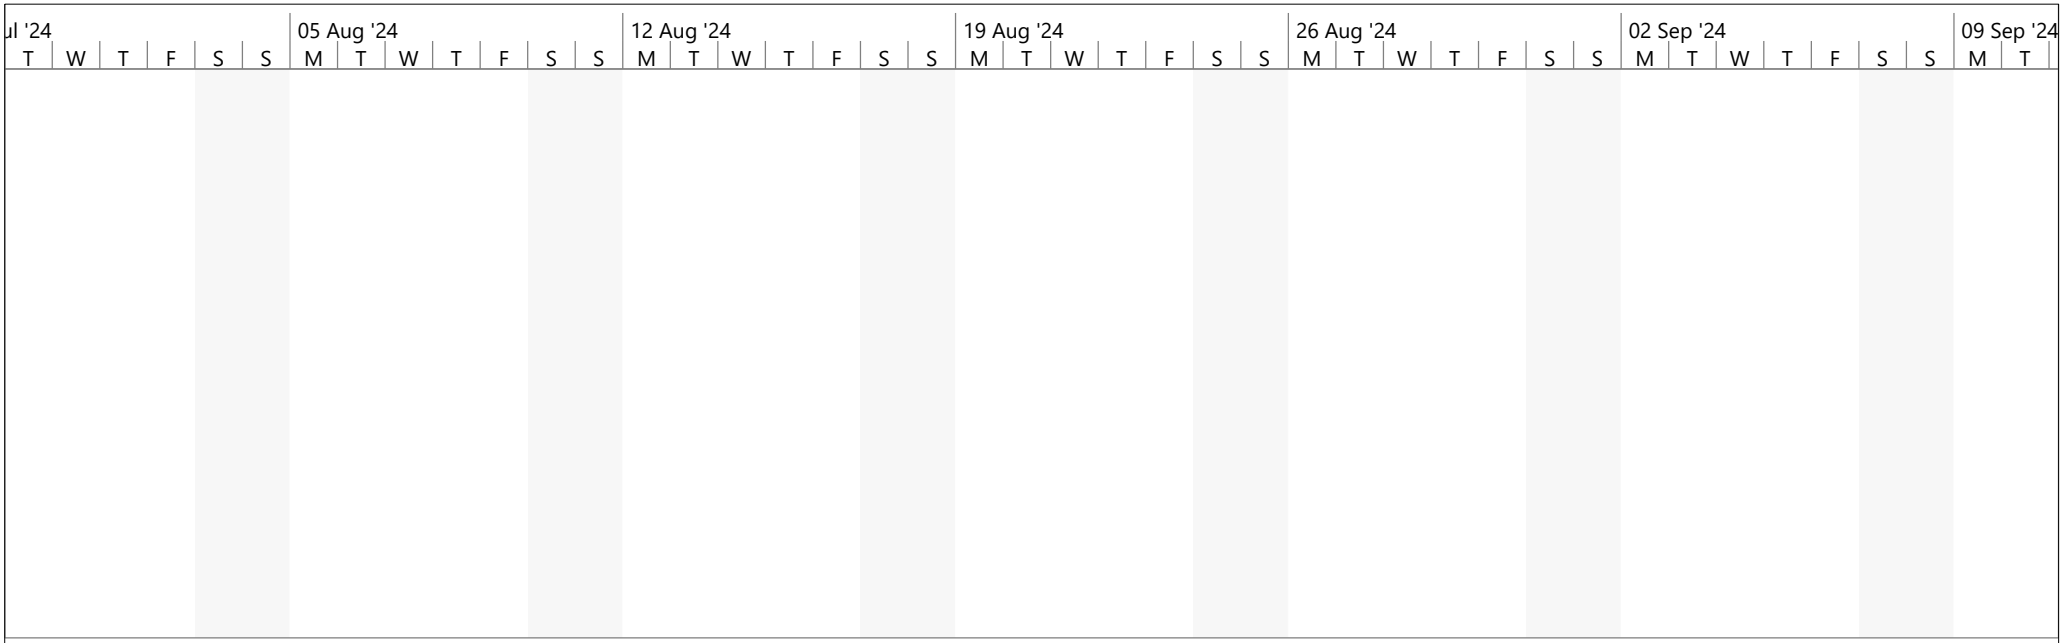

Project: plan projekta
Date: Thu 06/06/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

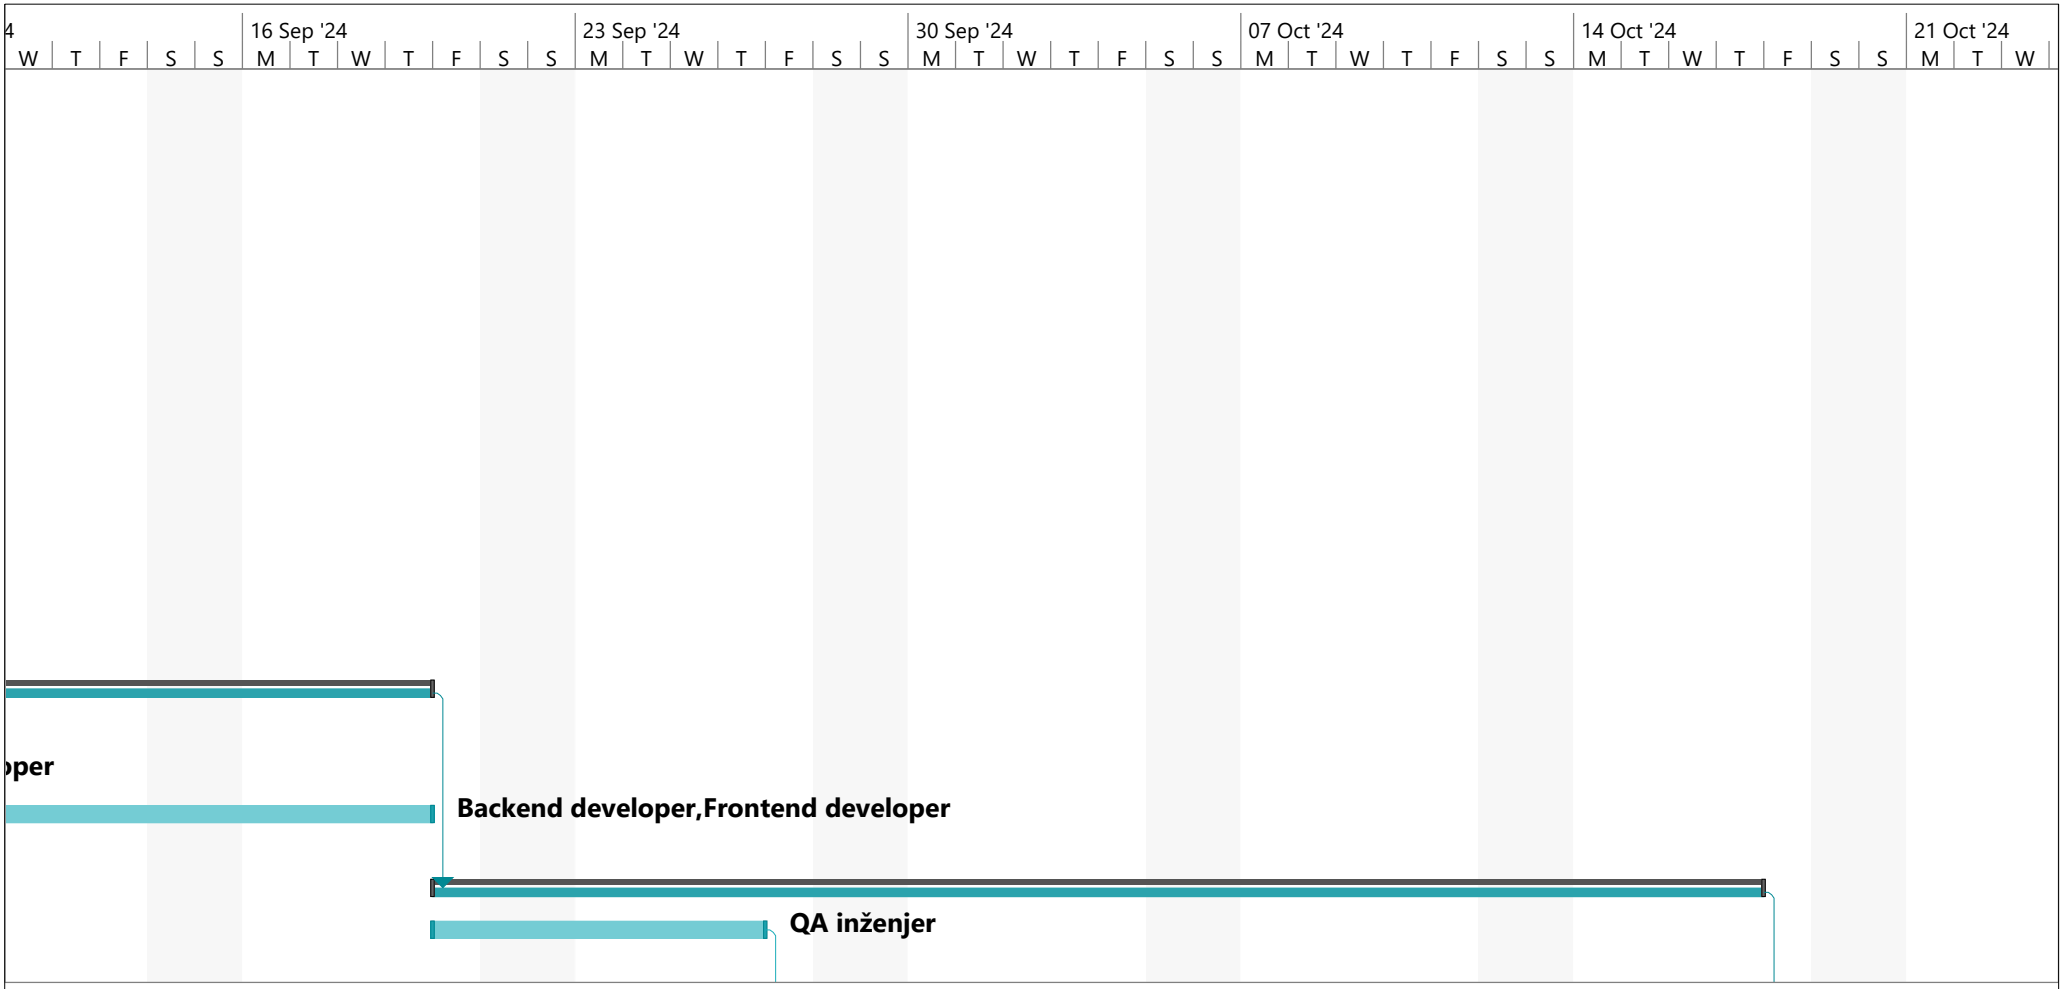

Project: plan projekta
Date: Thu 06/06/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

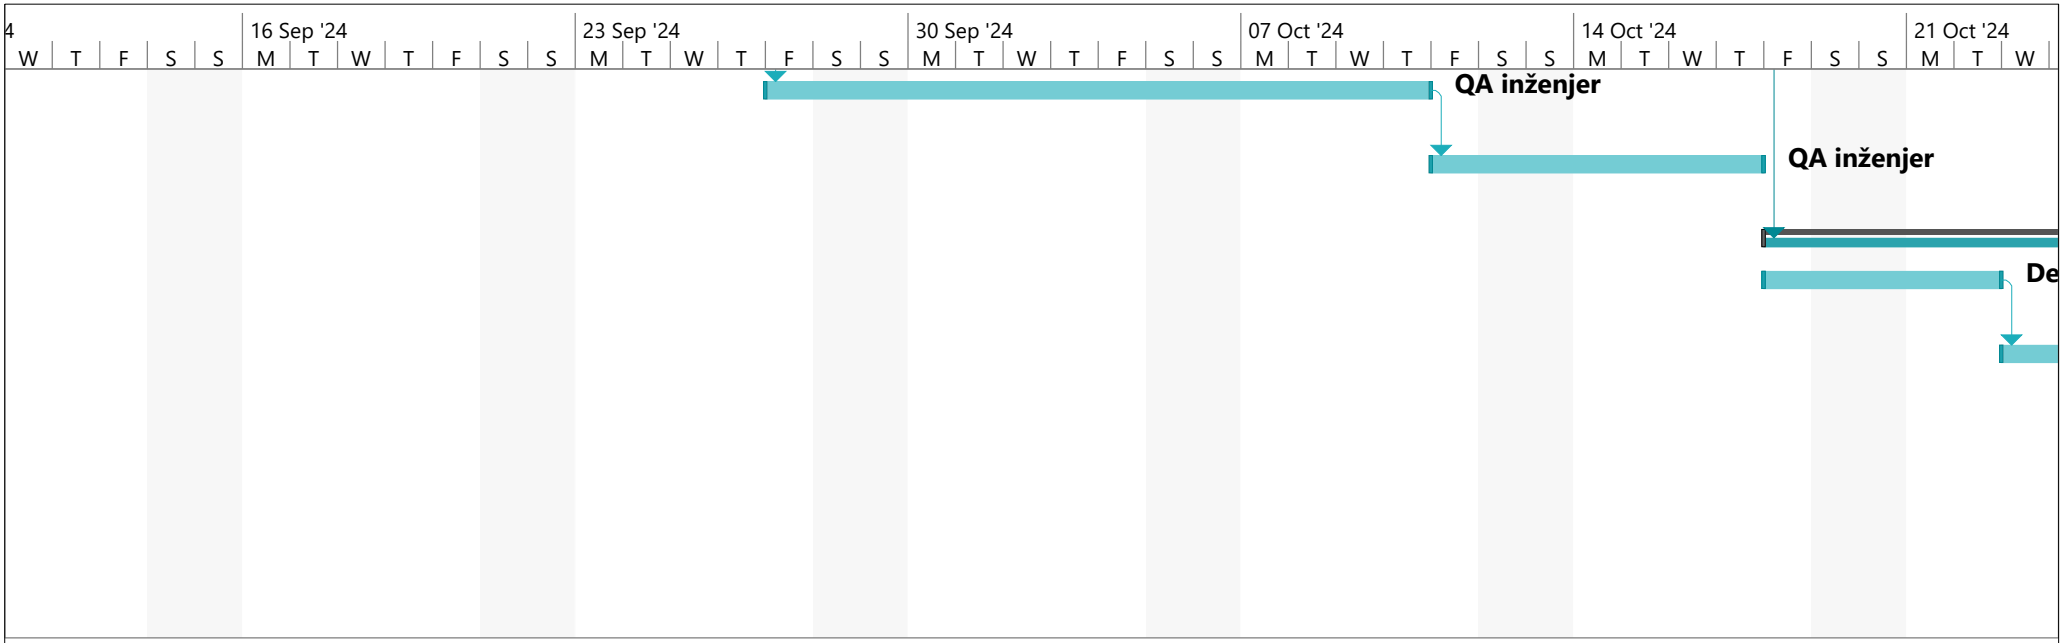

Project: plan projekta
Date: Thu 06/06/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Project: plan projekta
Date: Thu 06/06/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

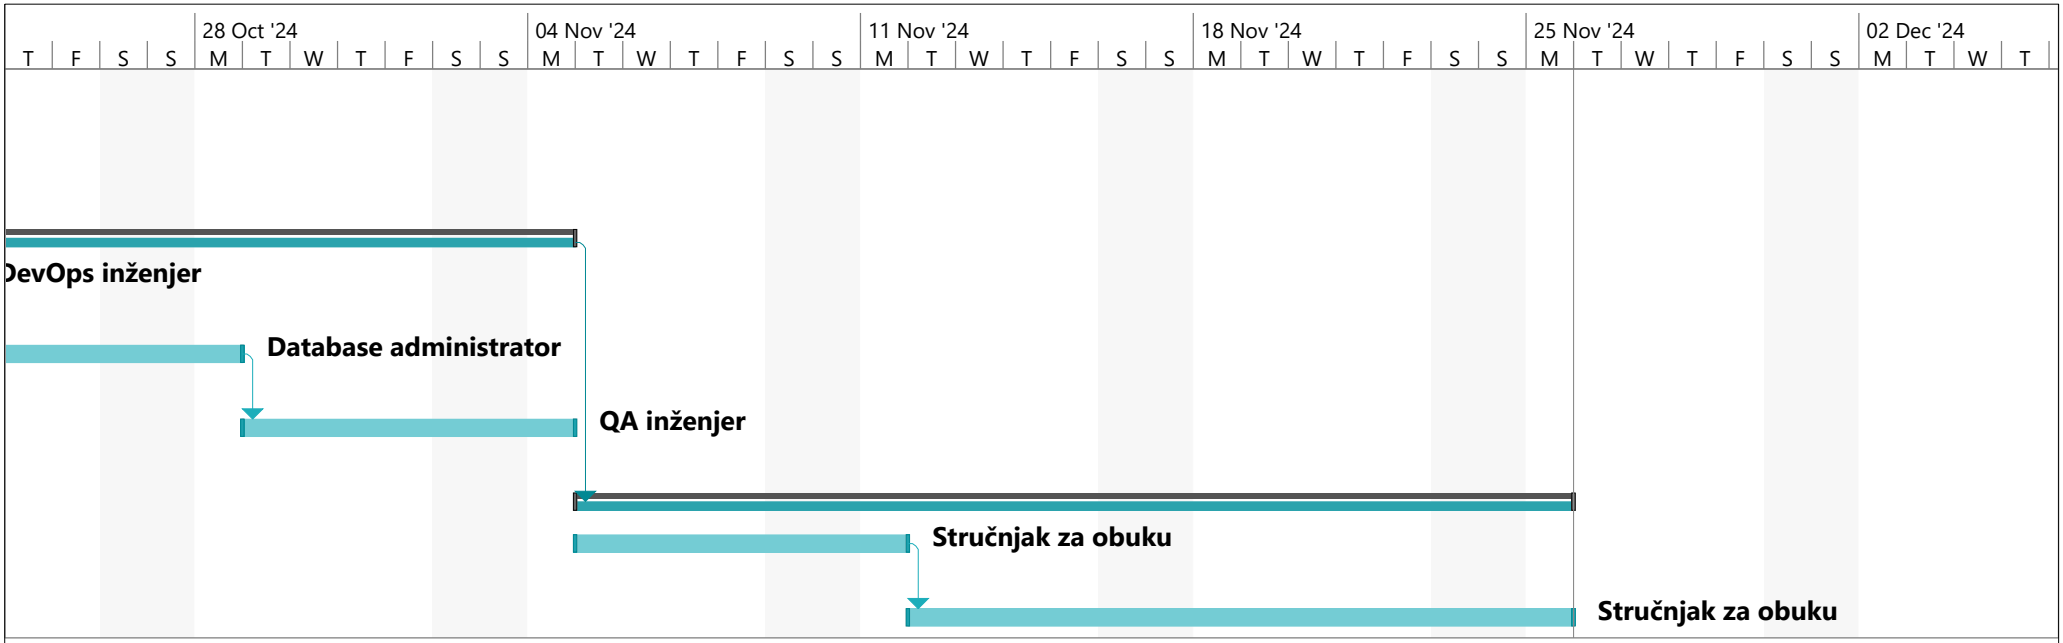

Project: plan projekta
Date: Thu 06/06/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
